


Figure 1. 12-month Gantt chart (start 1 Sep 2026, end 31 Aug 2027)

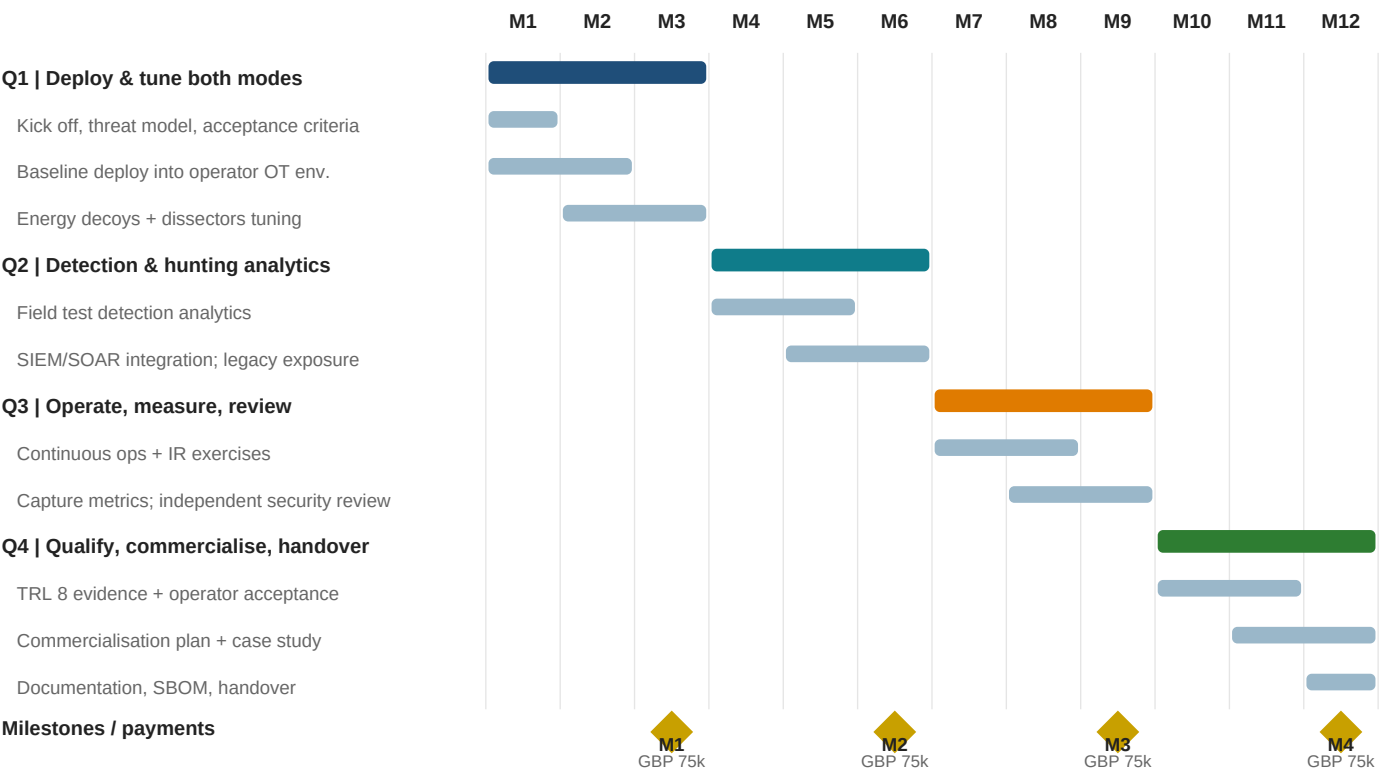

On site engagement:

Kick off (M1) | Mid project review (M6) | Final demonstration and handover (M12). Monthly remote delivery syncs throughout.

Total: GBP 300,000 (4 x GBP 75,000), no VAT. Matches the finance summary.

Table 1. SMART milestones, deliverables and payment schedule

Milestone	Month	Deliverable & SMART success criteria	Payment
M1 Foundation	M3	Both modes deployed and tuned in the operator's live OT environment; signed deployment and test plan; baseline detection demo against the real asset base.	GBP 75,000
M2 Analytics	M6	Detection and threat hunting analytics field tested; SIEM/SOAR integration; legacy exposure surfacing; interim metrics on detection rate and time to detect.	GBP 75,000
M3 Operate & assure	M9	Continuous operation and incident response exercises; success metrics captured (>=95% detection, <=1% false positive, <=5 min MTTD); independent security review.	GBP 75,000
M4 Qualify & handover	M12	TRL 8 qualification in environment; formal operator acceptance; commercialisation business model, plan and case study; documentation, SBOM and handover.	GBP 75,000
TOTAL (all inclusive, no VAT matches finance summary)			GBP 300,000

Management and evaluation

- Governance: monthly remote delivery syncs; quarterly go/no go gate at each milestone against the success criteria; shared, continuously maintained risk register.
- Evaluation: each milestone is signed off against adjudicated, measurable criteria; if a minimum metric is missed by more than 20%, scope is renegotiated jointly, not silently dropped.
- Accountability: Fatma Erturk (Founder & CEO) is accountable for delivery and is the single point of contact with Innovate UK and the energy operator. Work starts only after contract approval.
